Grand County and City of Moab Unified Transportation Master Plan
Updated: May 9, 2022
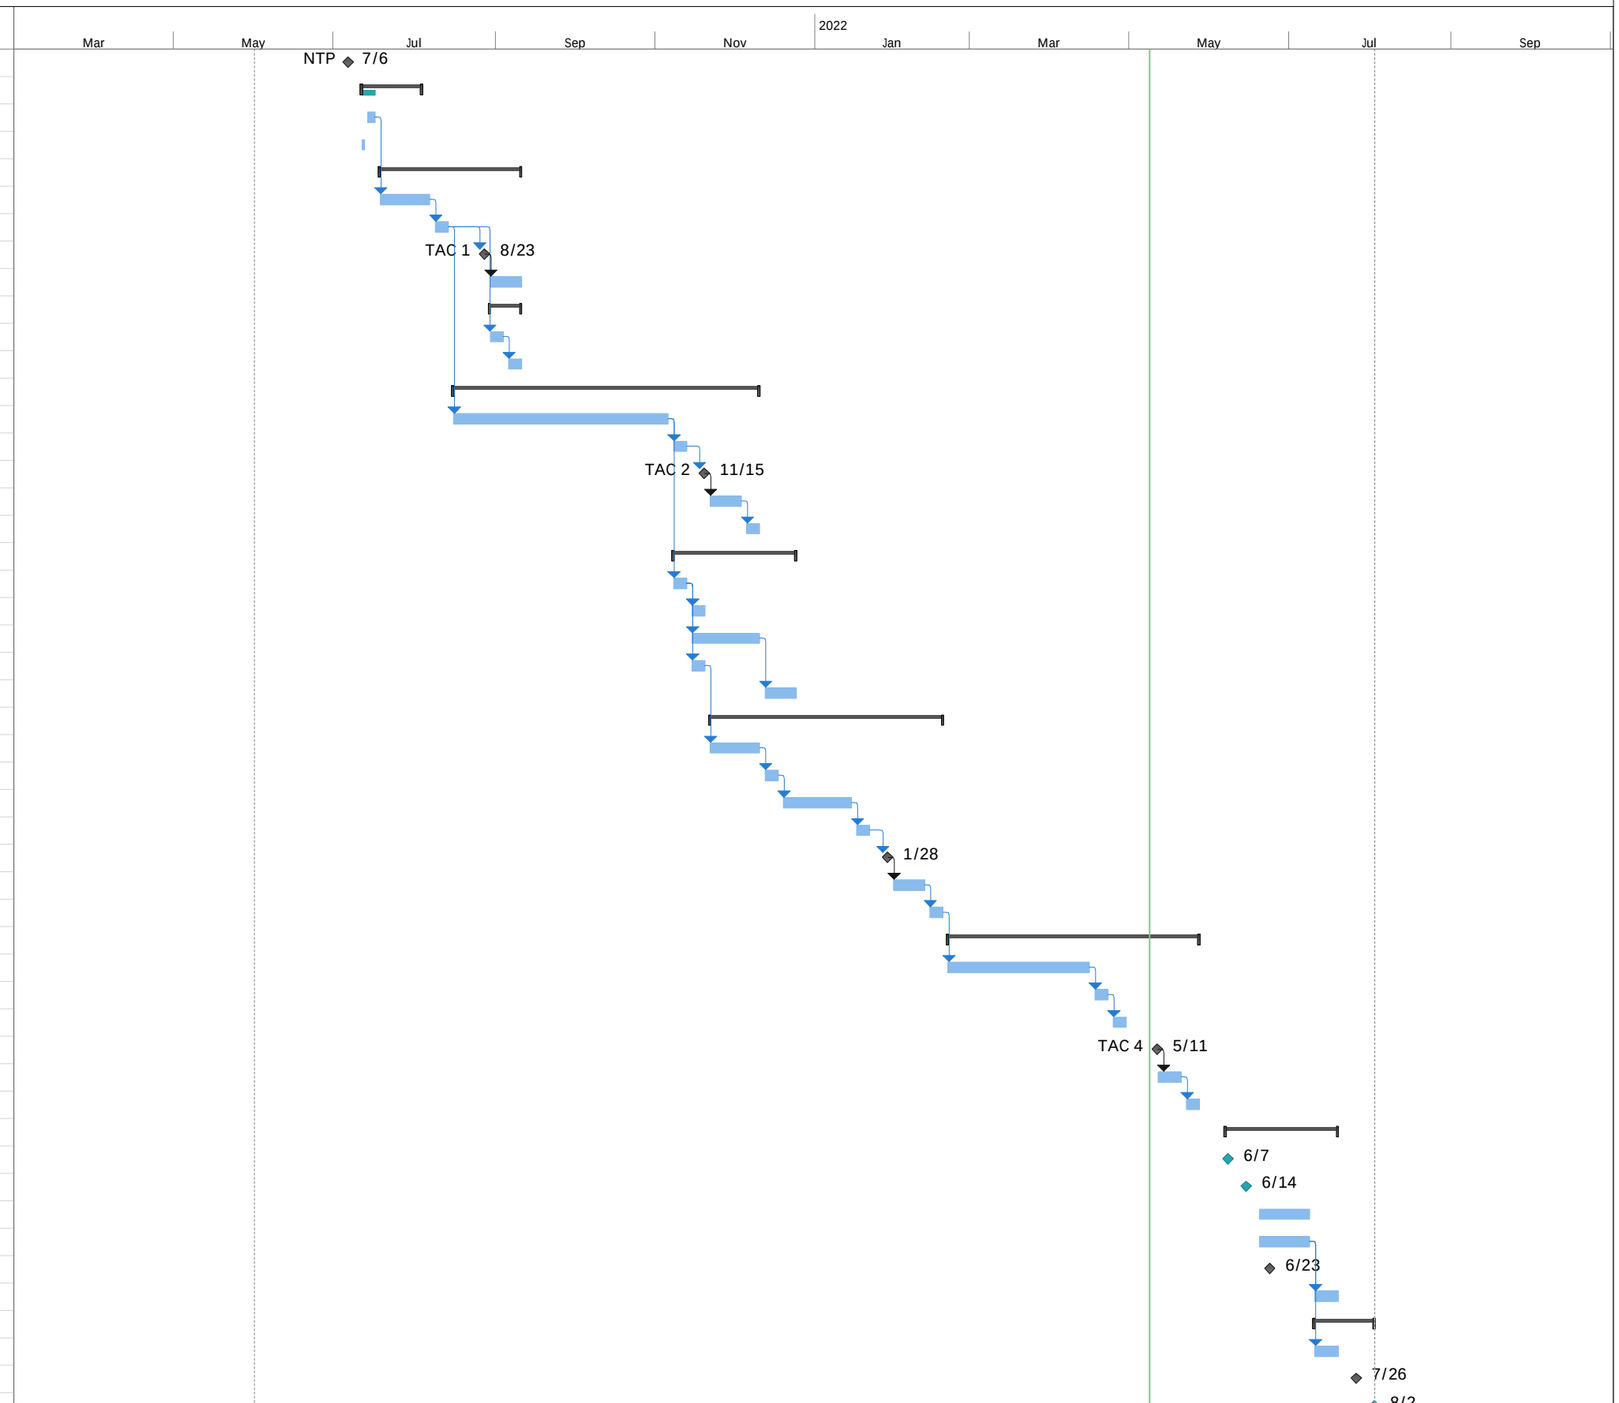
ID	Task Name	Start	Finish
1	Notice to Proceed	Tue 7/6/21	Tue 7/6/21
2	Work Task 1 - Project Management	Mon 7/12/21	Tue 8/3/21
3	Project Management Plan	Wed 7/14/21	Fri 7/16/21
4	Kick-Off Meeting	Mon 7/12/21	Mon 7/12/21
5	Work Task 2 - Previous Plans and Studies	Mon 7/19/21	Fri 9/10/21
6	Data Gathering, Plans and Studies Review	Mon 7/19/21	Fri 8/6/21
7	Inititial Needs Assessment Summary Memorandum	Mon 8/9/21	Fri 8/13/21
8	TAC Meeting No. 1	Mon 8/23/21	Fri 8/27/21
9	TAC Review Period	Mon 8/30/21	Fri 9/10/21
10	Work Task 3 - Stakeholder Interviews	Mon 8/30/21	Fri 9/10/21
11	Stakeholder Interviews	Mon 8/30/21	Fri 9/3/21
12	Stakeholder Interviews Summary Memorandum	Mon 9/6/21	Fri 9/10/21
13	Work Task 4 - Current and Future Conditions Analysis	Mon 8/16/21	Fri 12/10/21
14	Draft Working Paper No. 1 - Current and Future Conditions	Mon 8/16/21	Fri 11/5/21
15	PM Review / Address Comments	Mon 11/8/21	Fri 11/12/21
16	TAC Meeting No. 2	Mon 11/15/21	Fri 11/19/21
17	TAC Review Period	Mon 11/22/21	Fri 12/3/21
18	Final Working Paper No. 1 - Current and Future Conditions	Mon 12/6/21	Fri 12/10/21
19	Work Task 5 - Public Outreach Phase 1	Mon 11/8/21	Fri 12/24/21
20	Meeting Plan	Mon 11/8/21	Fri 11/12/21
21	Presentations (Stakeholder Groups, etc.)	Mon 11/15/21	Fri 11/19/21
22	On-Line Engagement	Mon 11/15/21	Fri 12/10/21
23	Community Meeting #1	Mon 11/15/21	Fri 11/19/21
24	Public Outreach Summary Report	Mon 12/13/21	Fri 12/24/21
25	Work Task 6 - Innovative Alternaives and Strategies Development	Mon 11/22/21	Fri 2/18/22
26	Toolbox Identification (Parking, ITS/Traffic/AM, Bike/Ped, Transit)	Mon 11/22/21	Fri 12/10/21
27	Toolbox Workshop / Community Meeting #2	Mon 12/13/21	Fri 12/17/21
28	Draft Working Paper No. 2 - Transportation Strategies	Mon 12/20/21	Fri 1/14/22
29	PM Review / Address Comments	Mon 1/17/22	Fri 1/21/22
30	TAC Meeting No. 3	Mon 1/24/22	Fri 1/28/22
31	TAC Review Period	Mon 1/31/22	Fri 2/11/22
32	Final Working Paper No. 2 - Transportation Strategies	Mon 2/14/22	Fri 2/18/22
33	Work Task 7 - Draft Transportation Master Plan	Mon 2/21/22	Fri 5/27/22
34	Transportation Master Plan Preparation	Mon 2/21/22	Fri 4/15/22
35	Draft TMP Submitted to PMT for review	Mon 4/18/22	Fri 4/22/22
36	Draft Transportation Master Plan to TAC	Mon 4/25/22	Fri 4/29/22
37	TAC Meeting No. 4	Wed 5/11/22	Wed 5/11/22
38	TAC Review Period	Thu 5/12/22	Fri 5/20/22
39	Final Draft TMP Preparation	Mon 5/23/22	Fri 5/27/22
40	Work Task 8 - Community Outreach - Draft Plan	Tue 6/7/22	Tue 7/19/22
41	County Commission Meeting	Tue 6/7/22	Tue 6/7/22
42	City Council	Tue 6/14/22	Tue 6/14/22
43	Draft UTMP Posted for Public Review	Mon 6/20/22	Fri 7/8/22
44	Public Comment Period	Mon 6/20/22	Fri 7/8/22
45	Community Meeting #3	Thu 6/23/22	Thu 6/23/22
46	Public Outreach Summary Report	Mon 7/11/22	Tue 7/19/22
47	Task 9 - Final Transportation Master Plan	Mon 7/11/22	Tue 8/2/22
48	Final Transportation Master Plan	Mon 7/11/22	Tue 7/19/22
49	City Council Presentation	Tue 7/26/22	Tue 7/26/22
50	Grand County Commission Presentation	Tue 8/2/22	Tue 8/2/22
